


Main works update



Main works Schedule 17 Lorry routes application

- Submitted 16 September, extension for decision to 20 December agreed (Committee 19 December)
- Application requests approval of a list of routes to and from Euston Approaches work site and Adelaide Road work site
- Schedule 17 does not specify the numbers of lorry movements, only the routes that can be used
- Letter of clarification sent to Camden Council confirming that the proposed scheme is the 'developed design'
- The predicted LGV numbers are below those assessed in the Environmental Statement
- The Local Traffic Management Plan (LTMP) outlines details such as highway closures and work site access /egress points and describes mitigation measures (e.g. haul roads, vehicle holding areas, speed limits etc) to reduce impacts on residential streets
- The LTMP will be periodically updated to review and adapt mitigation measures as appropriate

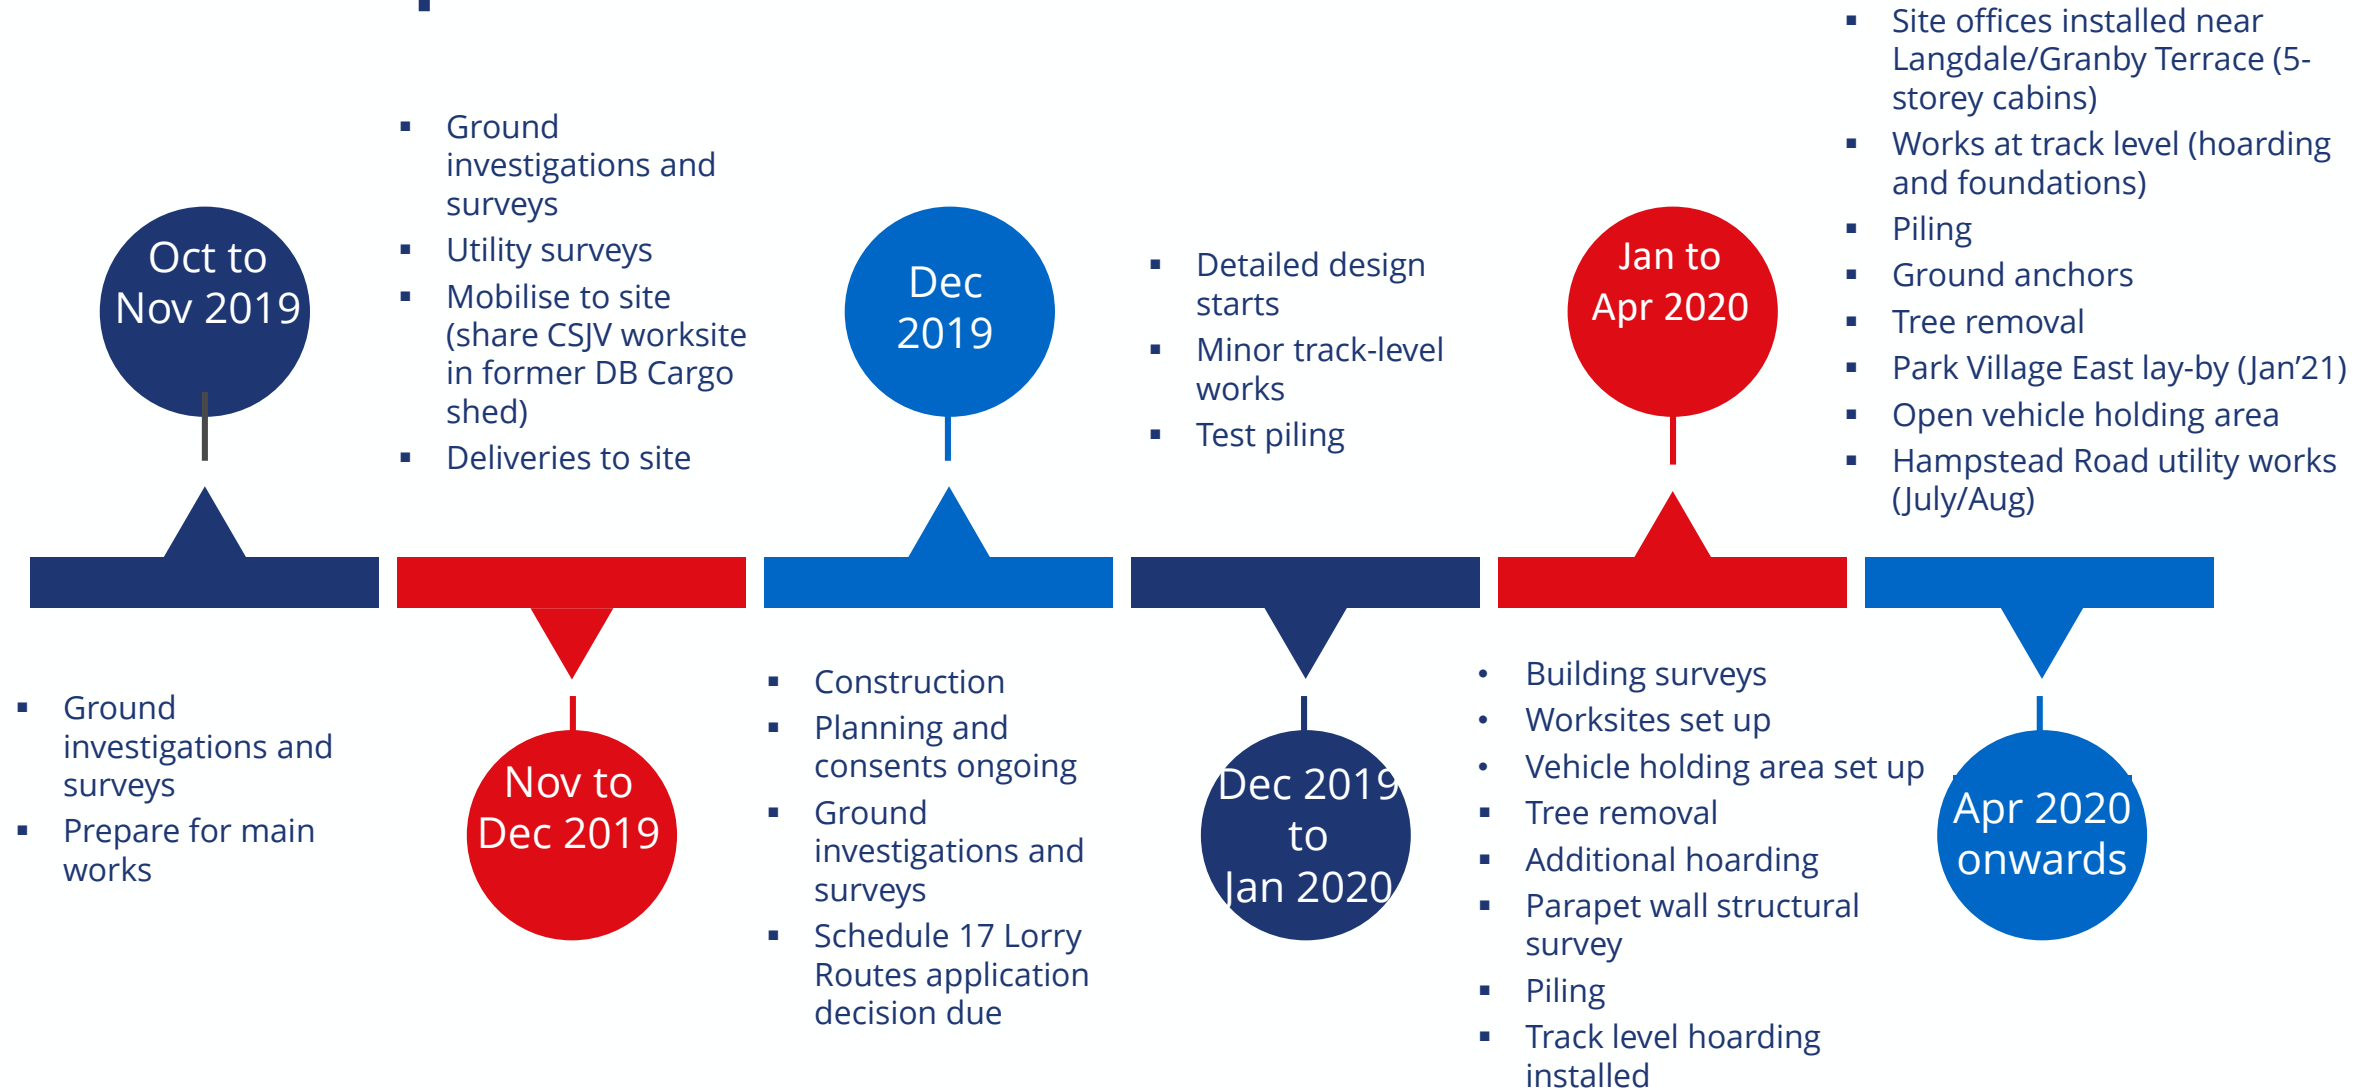

Lorry routes for main works – providing access to the sites

Phase one: Until August 2020

Constraints

- Park Village East northern end closed;
- Hampstead Road access point under construction. Will be used as soon as access is complete;

Granby Terrace Bridge access

Lorry route:


- In - along Hampstead Road, left into Granby Terrace;
- Out - right from Granby Terrace Bridge onto Hampstead Road;

Stanhope Street access to be used only for large loads over 40 tonnes that can't use Granby Terrace Bridge

Hampstead Road access point under construction will be used as soon as access is complete;

Lorry route:

- In - along Hampstead Road, left into Granby Terrace;
- Out - right from Granby Terrace Bridge onto Hampstead Road;

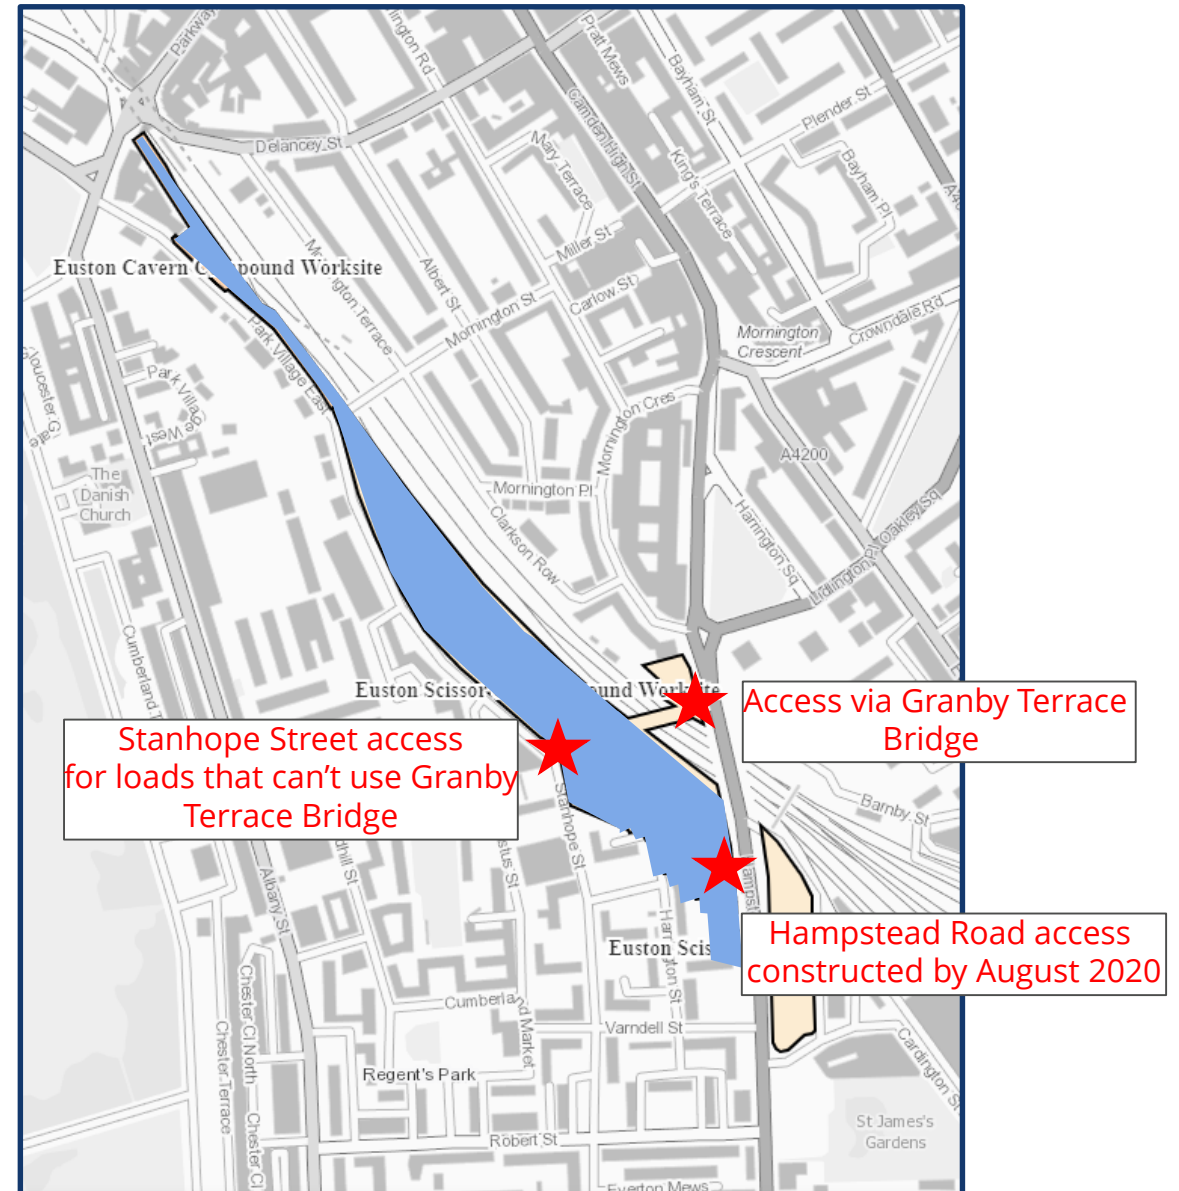

Lorry routes for main works – providing access to the sites

Phase two: August 2020 until January 2022

Cavern access at Park Village East street level in use from January 2021, materials lifted down to track level.

Lorry route:

- In - Albany Street, Park Village East;
- Out - Park Village East, Mornington Street/Terrace, Delancey Street, Gloucester Gate, Albany Street.

Hampstead Road access and haul road in use for access to blue area, for works up to and including Granby Terrace Bridge – duration to be confirmed,

Lorry route:

- In – left from Hampstead Road
- Out - right onto Hampstead Road (subject to TfL approval)

Stanhope Street access in use for works within pink area,


Lorry route:

- In - Hampstead Road, Robert Street, Stanhope Street;
- Out - Stanhope Street, Robert Street, Hampstead Road.

Work on the construction of the Granby Terrace Bridge extension prevents vehicles travelling from Hampstead Road access into the pink area

Granby Terrace access not available for construction traffic during bridge works

Opportunity to extend the use of the haul road to all areas is being explored

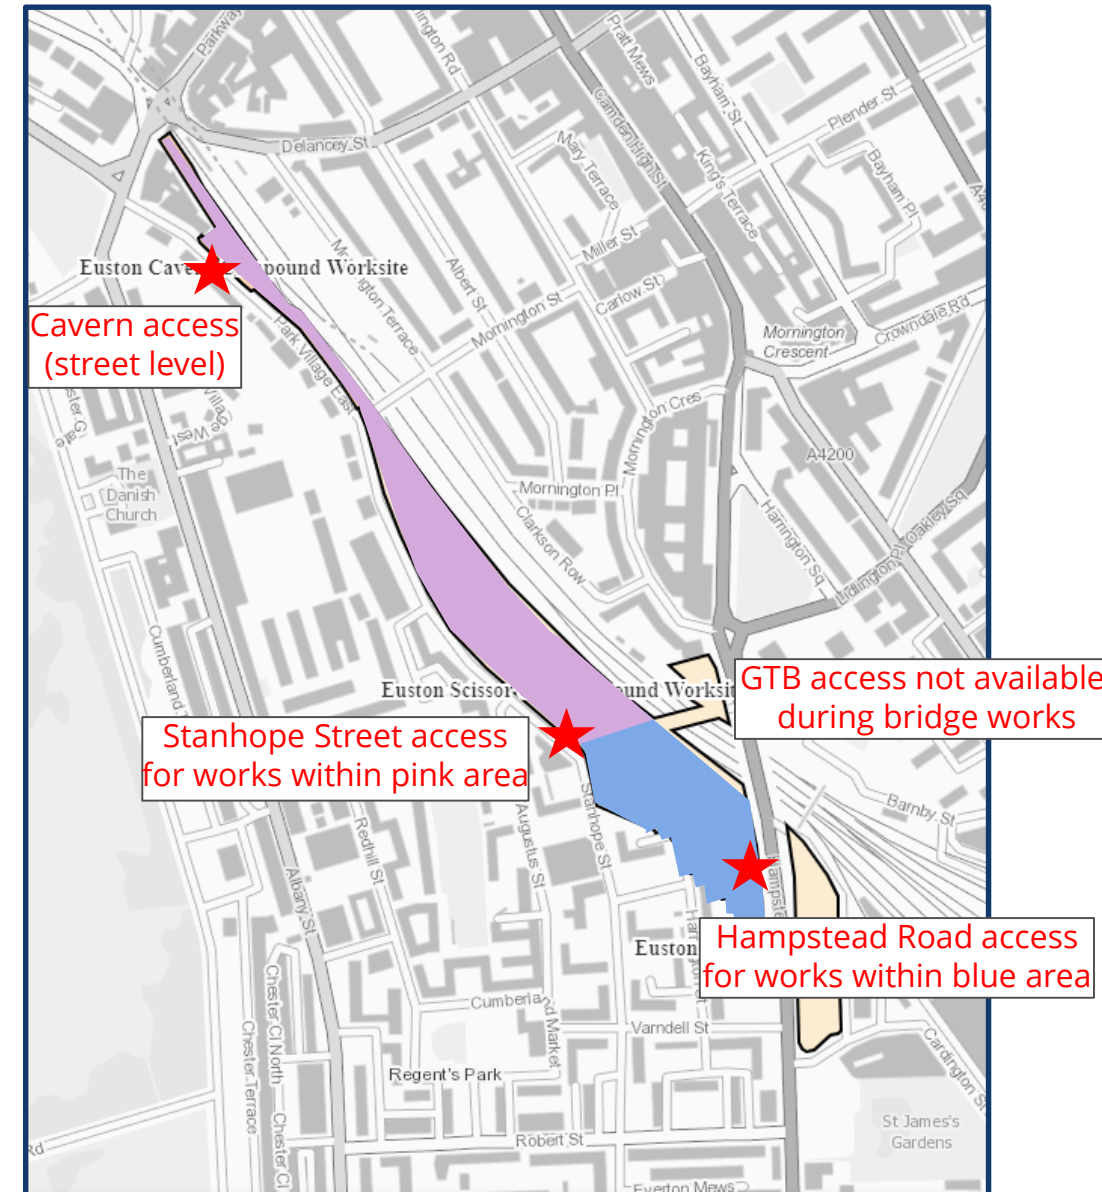

Lorry routes for main works – providing access to the sites

Phase three: January 2022 until March 2026

Cavern access at Park Village East street level, materials lifted down to track level.

Lorry route:

- In - Albany Street, Park Village East
- Out - Park Village East, Mornington Street/Terrace, Delancey Street, Gloucester Gate, Albany Street.


Hampstead Road access and haul road in use,

Lorry route:

- In - left from Hampstead Road
- Out - right onto Hampstead Road

Granby Terrace Bridge access 'in' only for works in the pink area

Stanhope Street access only for loads over 40 tonnes that cannot use Granby Terrace Bridge

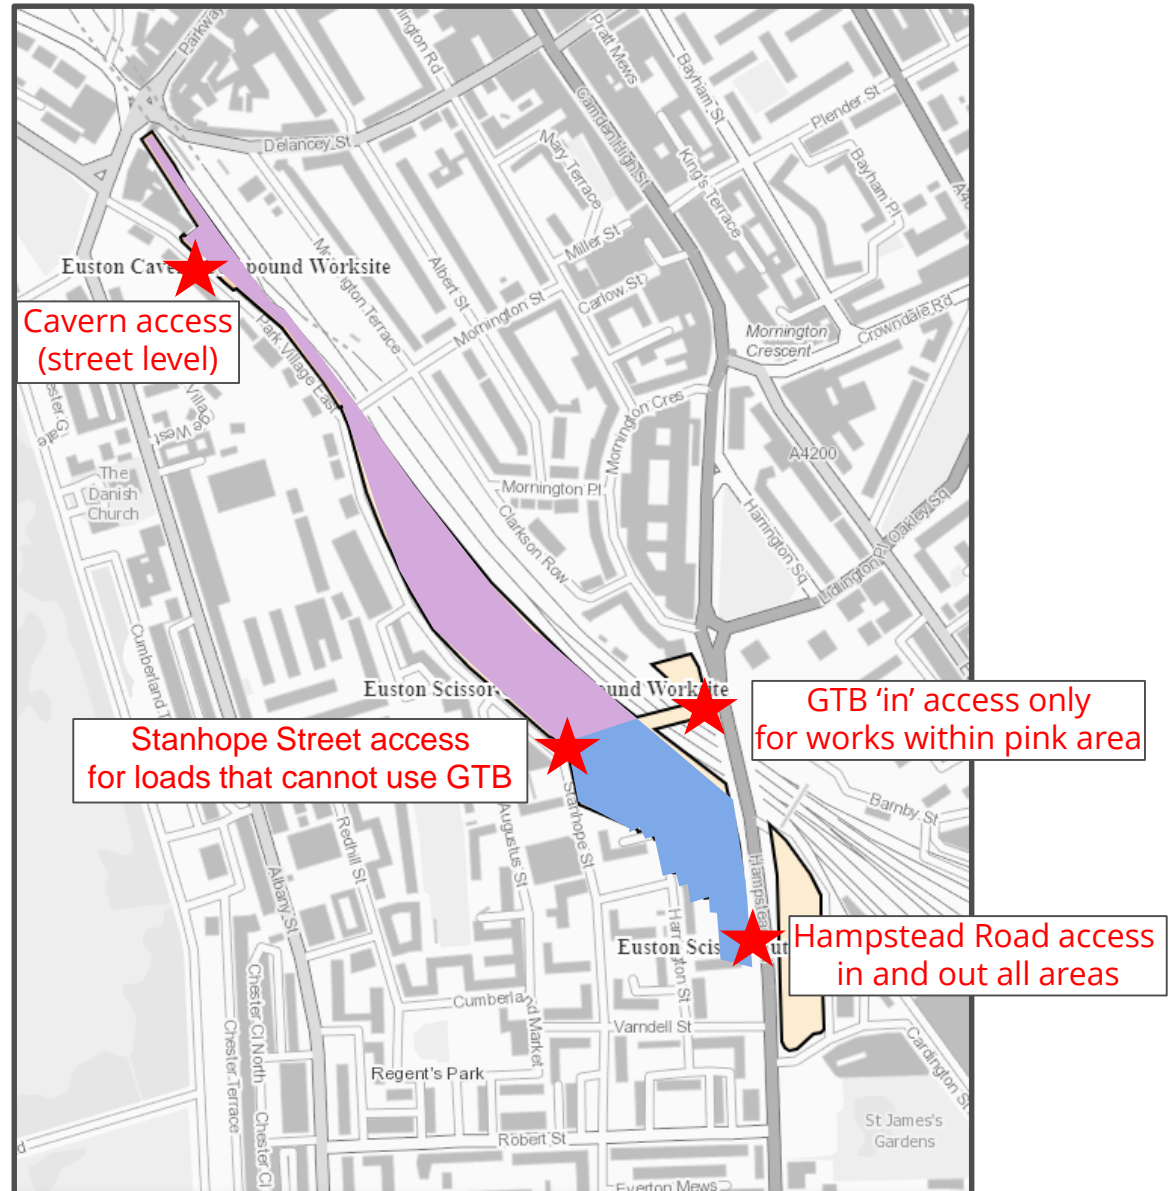

Lorry routes for main works – providing access to the sites

Phase four: **Four weeks only** in January 2023 & August 2024 (Hampstead Road Bridge closed)

Cavern access at Park Village East street level, materials lifted down to track level.

Lorry route:

- In - Albany Street, Park Village East
- Out - Park Village East, Mornington Street/Terrace, Delancey Street, Gloucester Gate, Albany Street.

Stanhope Street access in use for all works between Hampstead Road and the cavern, excluding works on the Hampstead Road Bridge itself.

Lorry route:

- In - Hampstead Road, Robert Street, Stanhope Street;
- Out - Stanhope Street, Robert Street, Hampstead Road.

Hampstead Road access for Hampstead Road Bridge works only due to construction works preventing vehicles accessing Euston Approaches area. Works include piling and lifting bridge beams into place.

